




Music and Drama Center Demolition Schedule

January 3	Begin destructive hazardous material testing
January 13	City reviews Perimeter Transition Area (PTA) application
March 15 to April 30	Asbestos and hazardous material abatement
April 4 to May 4	Bid demolition and contractor selection
May 15-31	Building available for City of Northfield training
June 20	Begin demolition
September 15	Demolition complete
October 31	Site work restoration and project complete

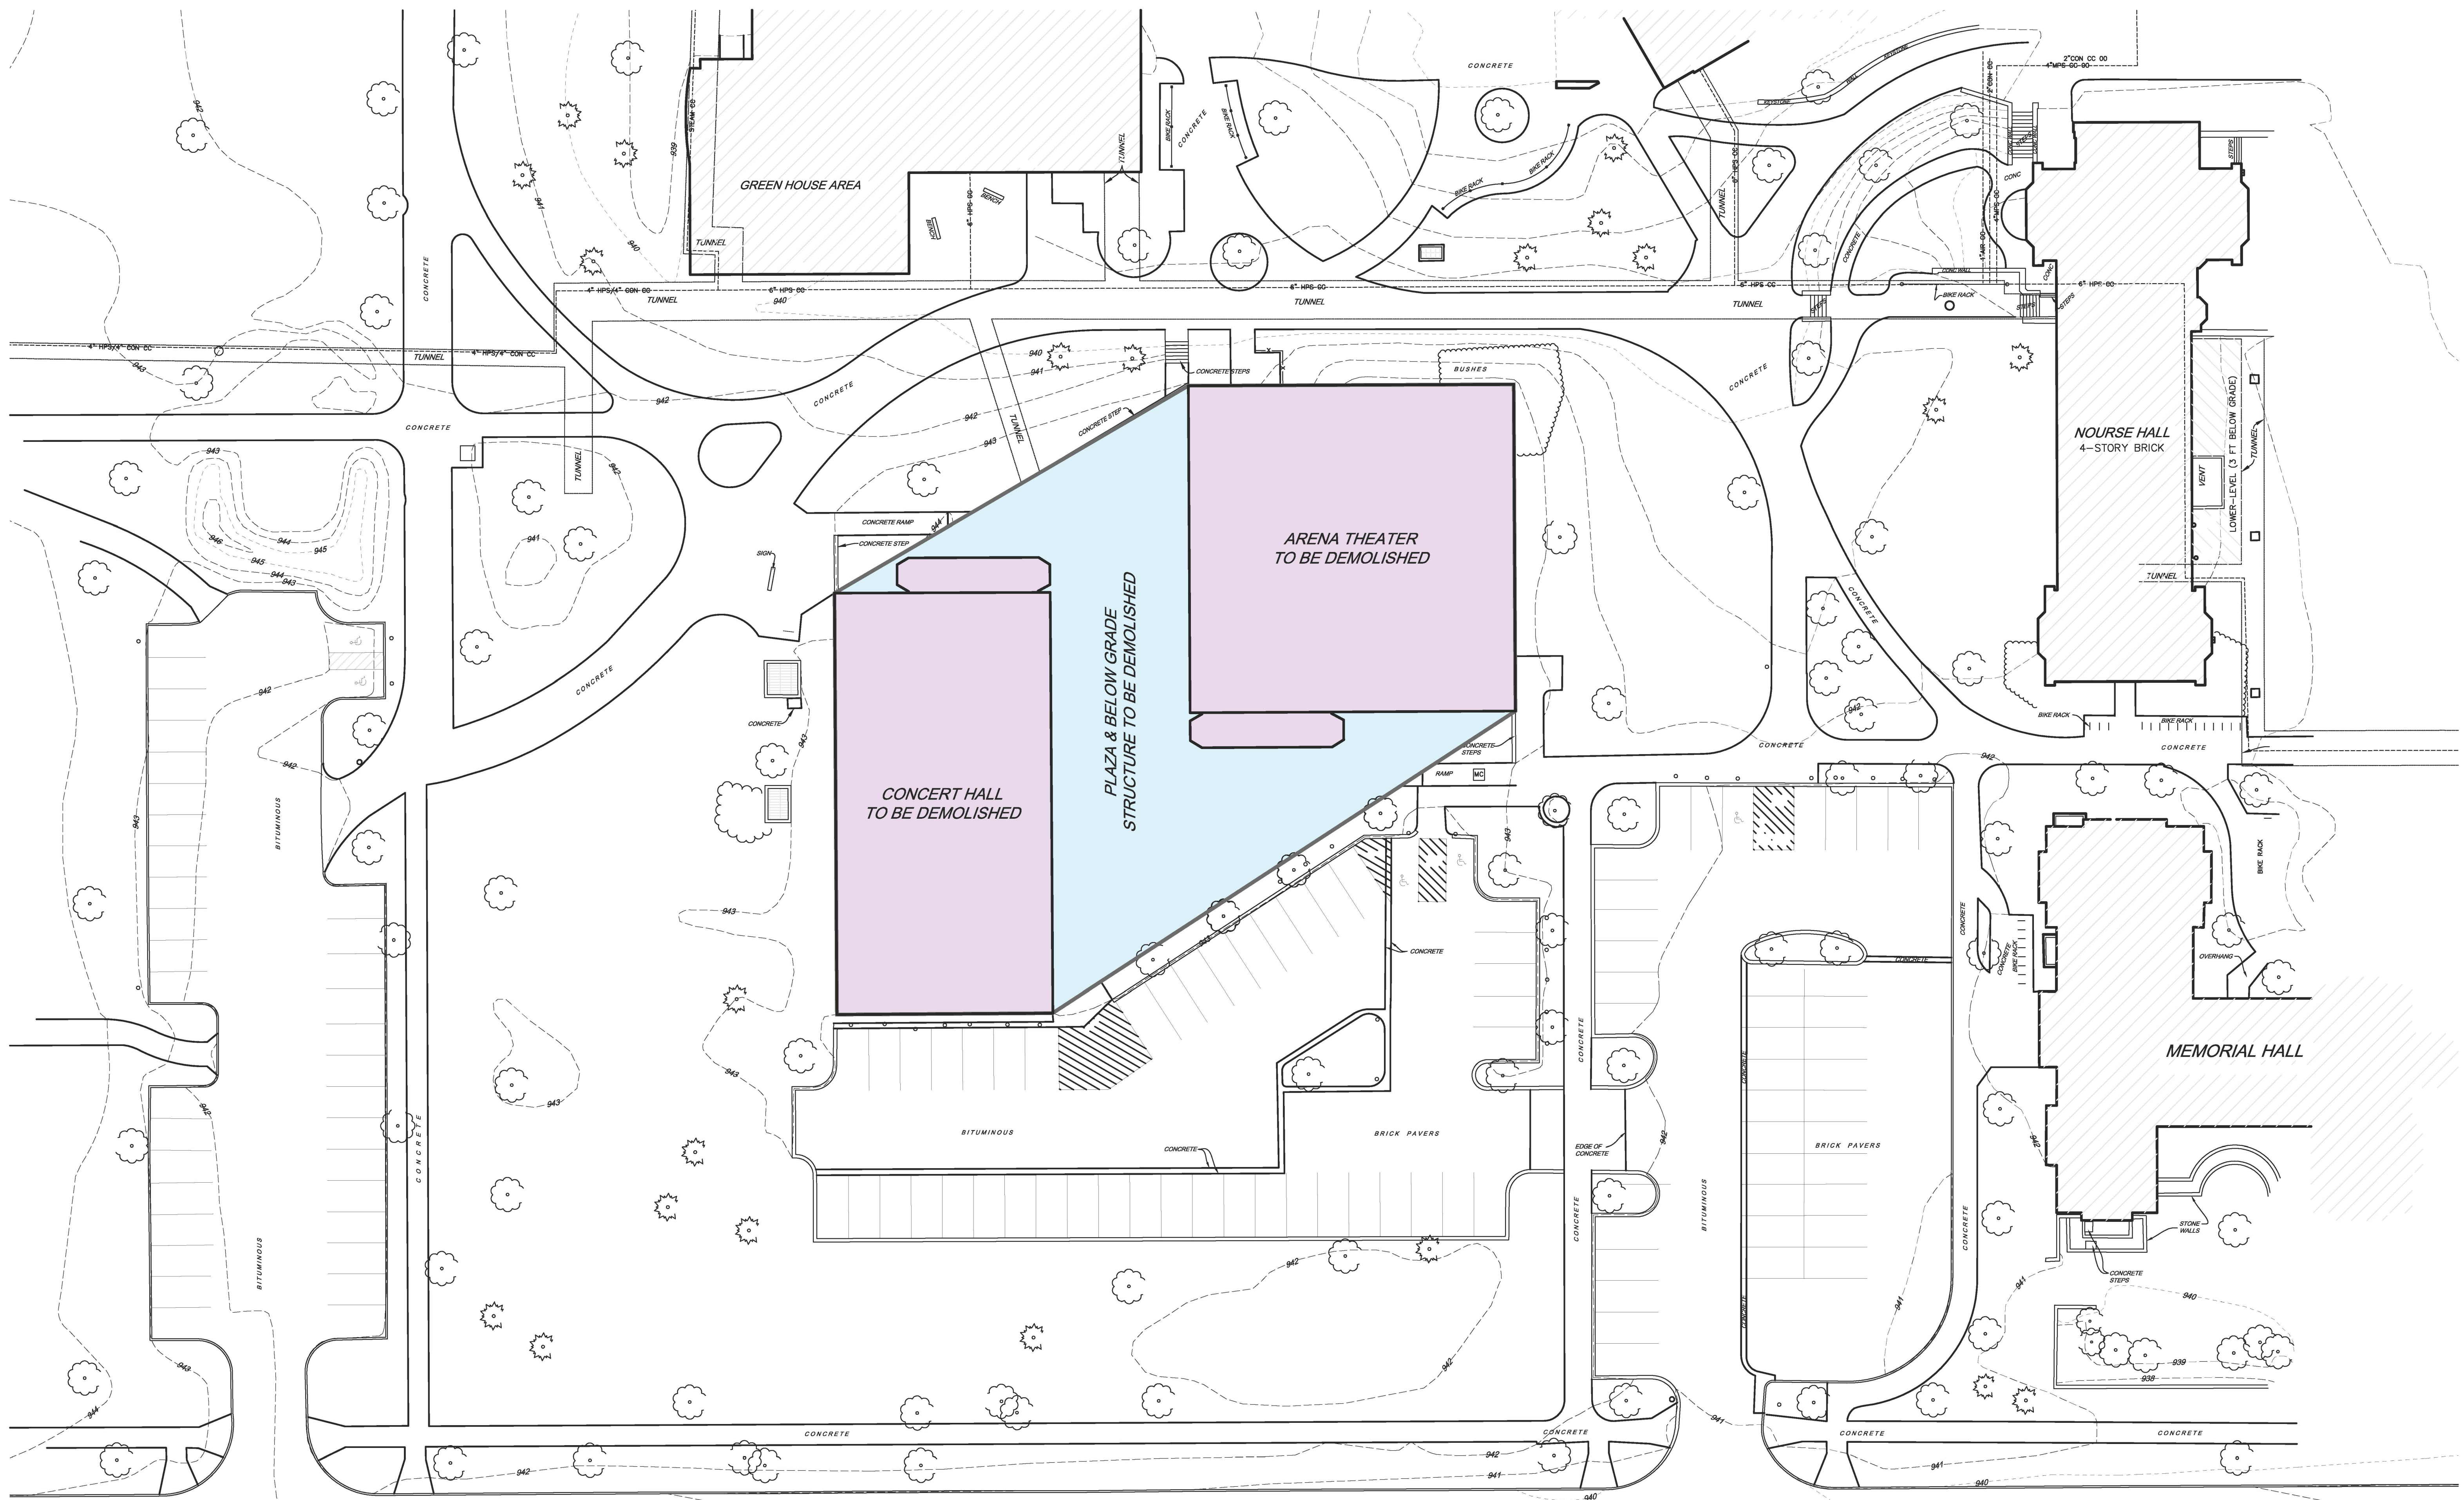


FIRST STREET

WINONA STREET

NEVADA STREET

 **Existing Site Plan**

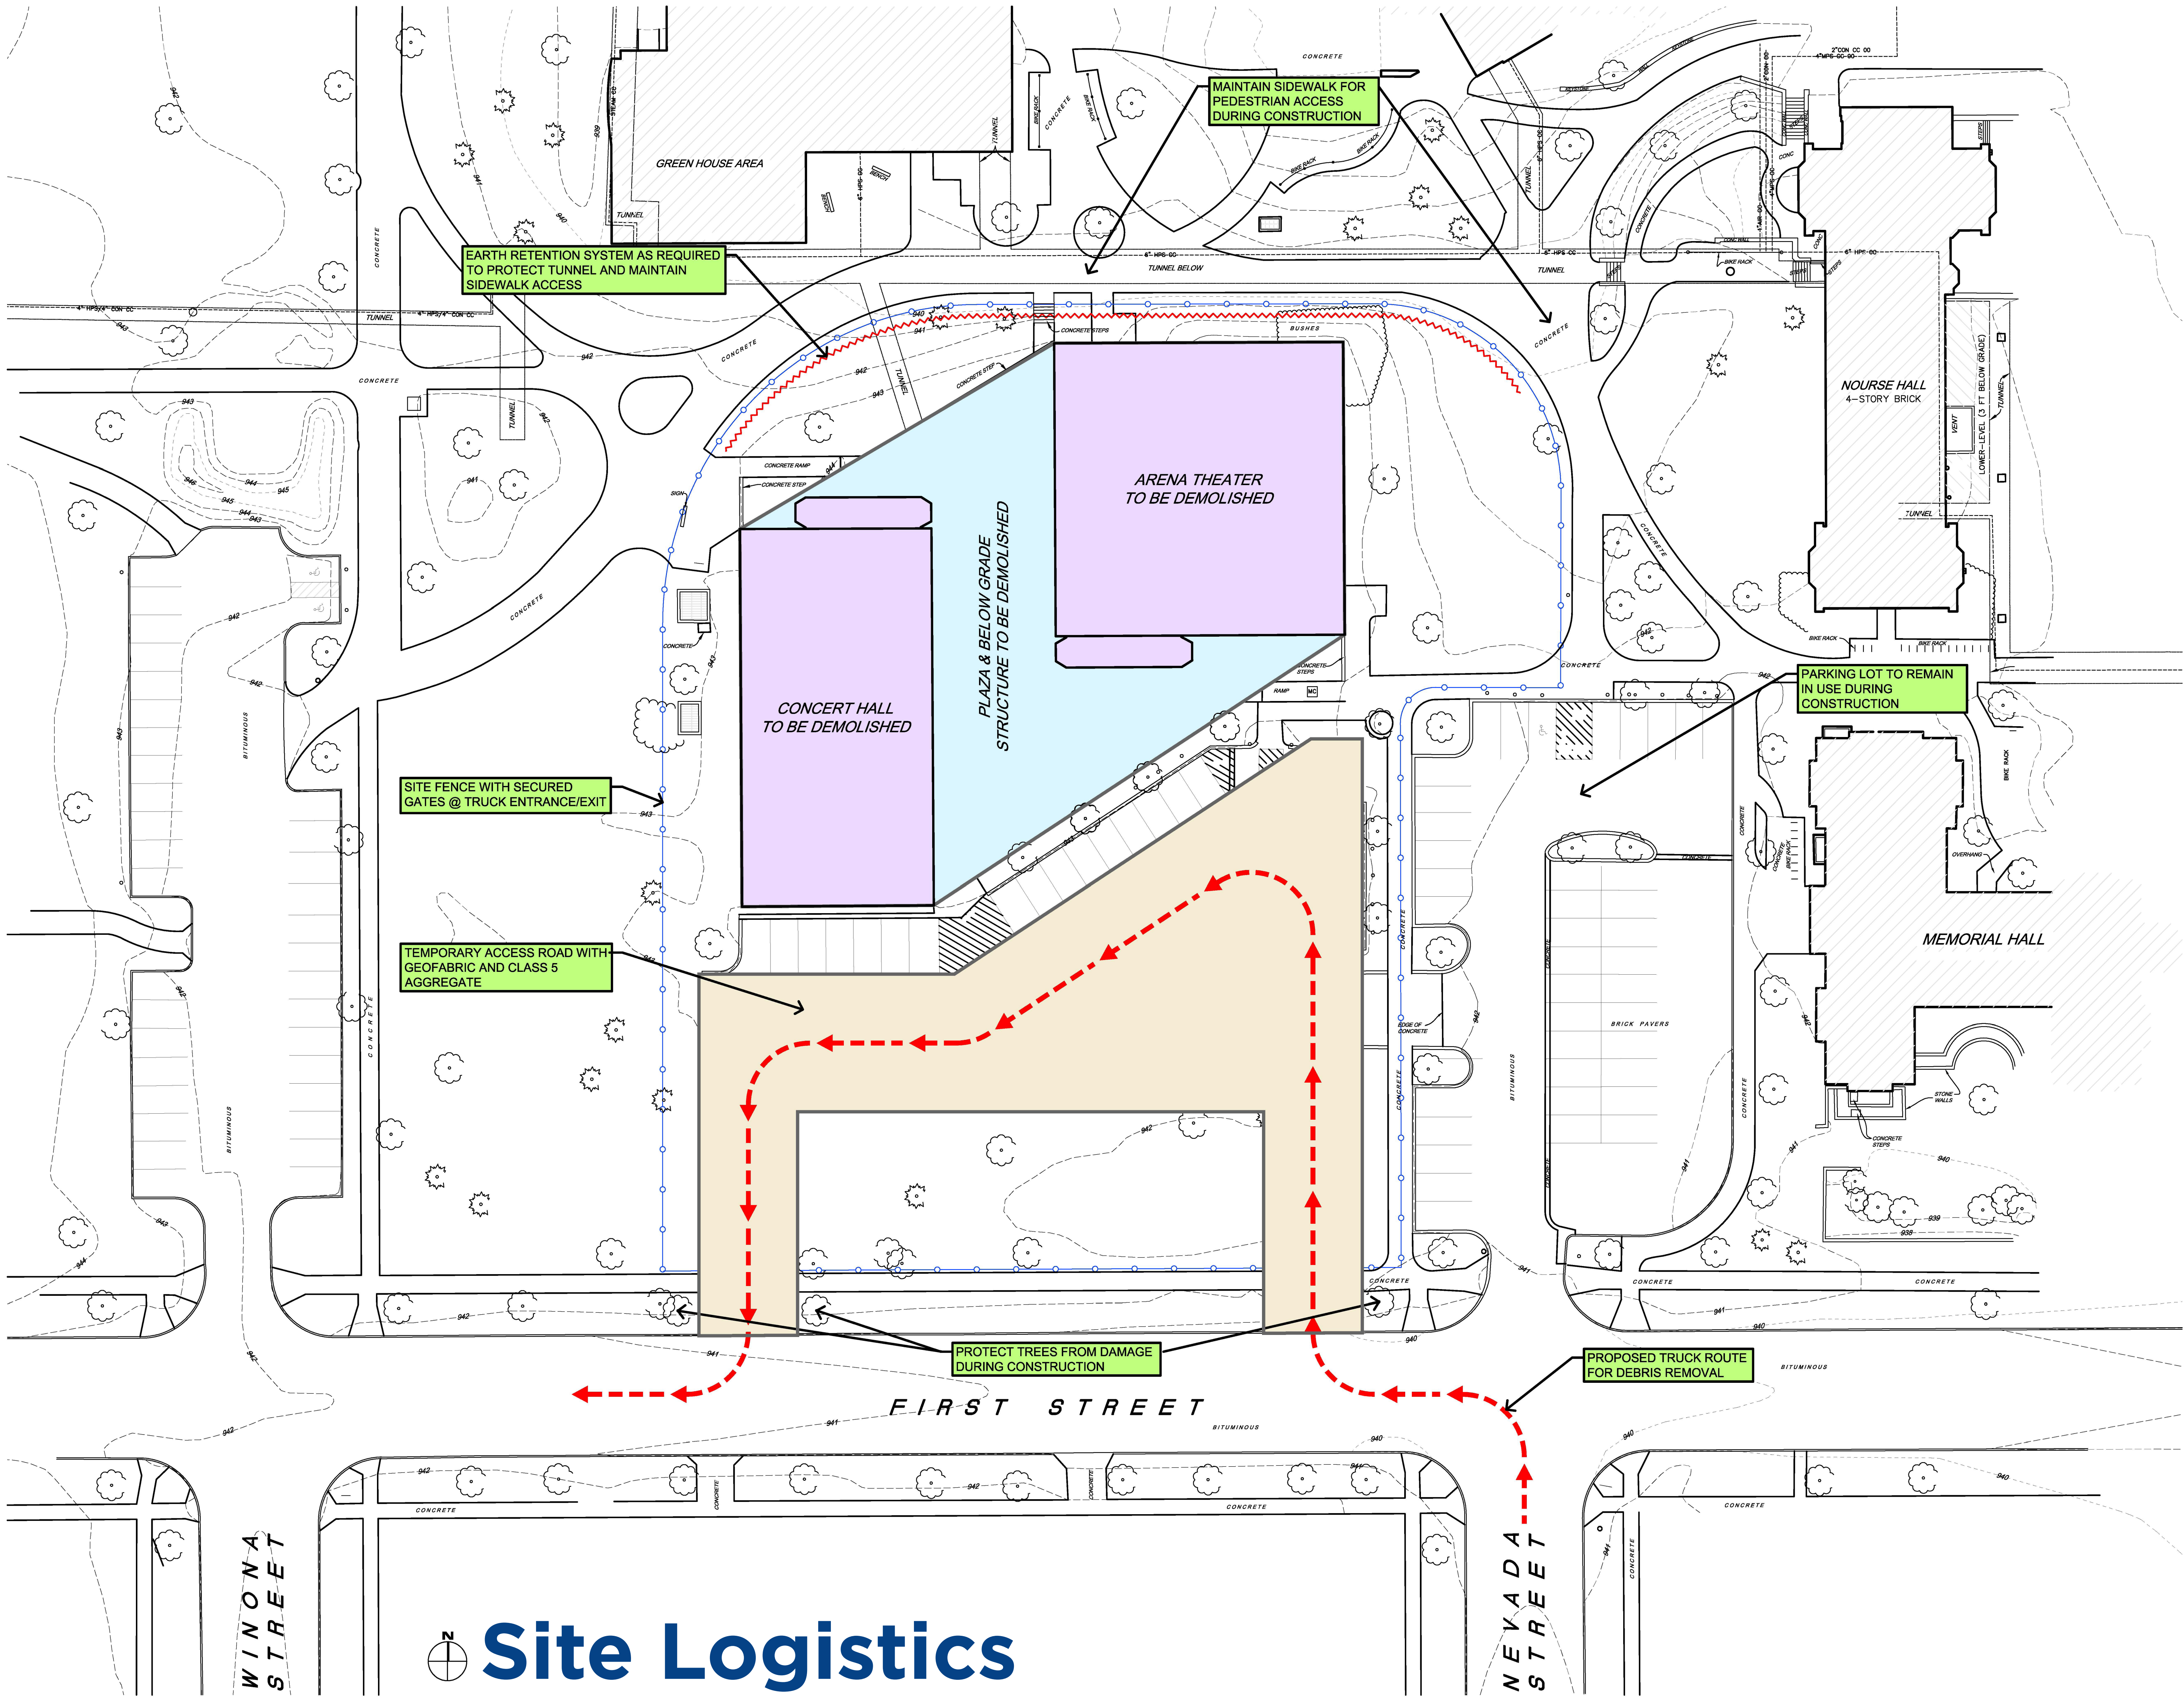

SITE FENCE WITH SECURED GATES @ TRUCK ENTRANCE/EXIT

TEMPORARY ACCESS ROAD WITH GEOFABRIC AND CLASS 5 AGGREGATE

PROTECT TREES FROM DAMAGE DURING CONSTRUCTION

MAINTAIN SIDEWALK FOR PEDESTRIAN ACCESS DURING CONSTRUCTION

PARKING LOT TO REMAIN IN USE DURING CONSTRUCTION


PROPOSED TRUCK ROUTE FOR DEBRIS REMOVAL

Site Logistics

WINONA STREET

FIRST STREET

NEVADA STREET

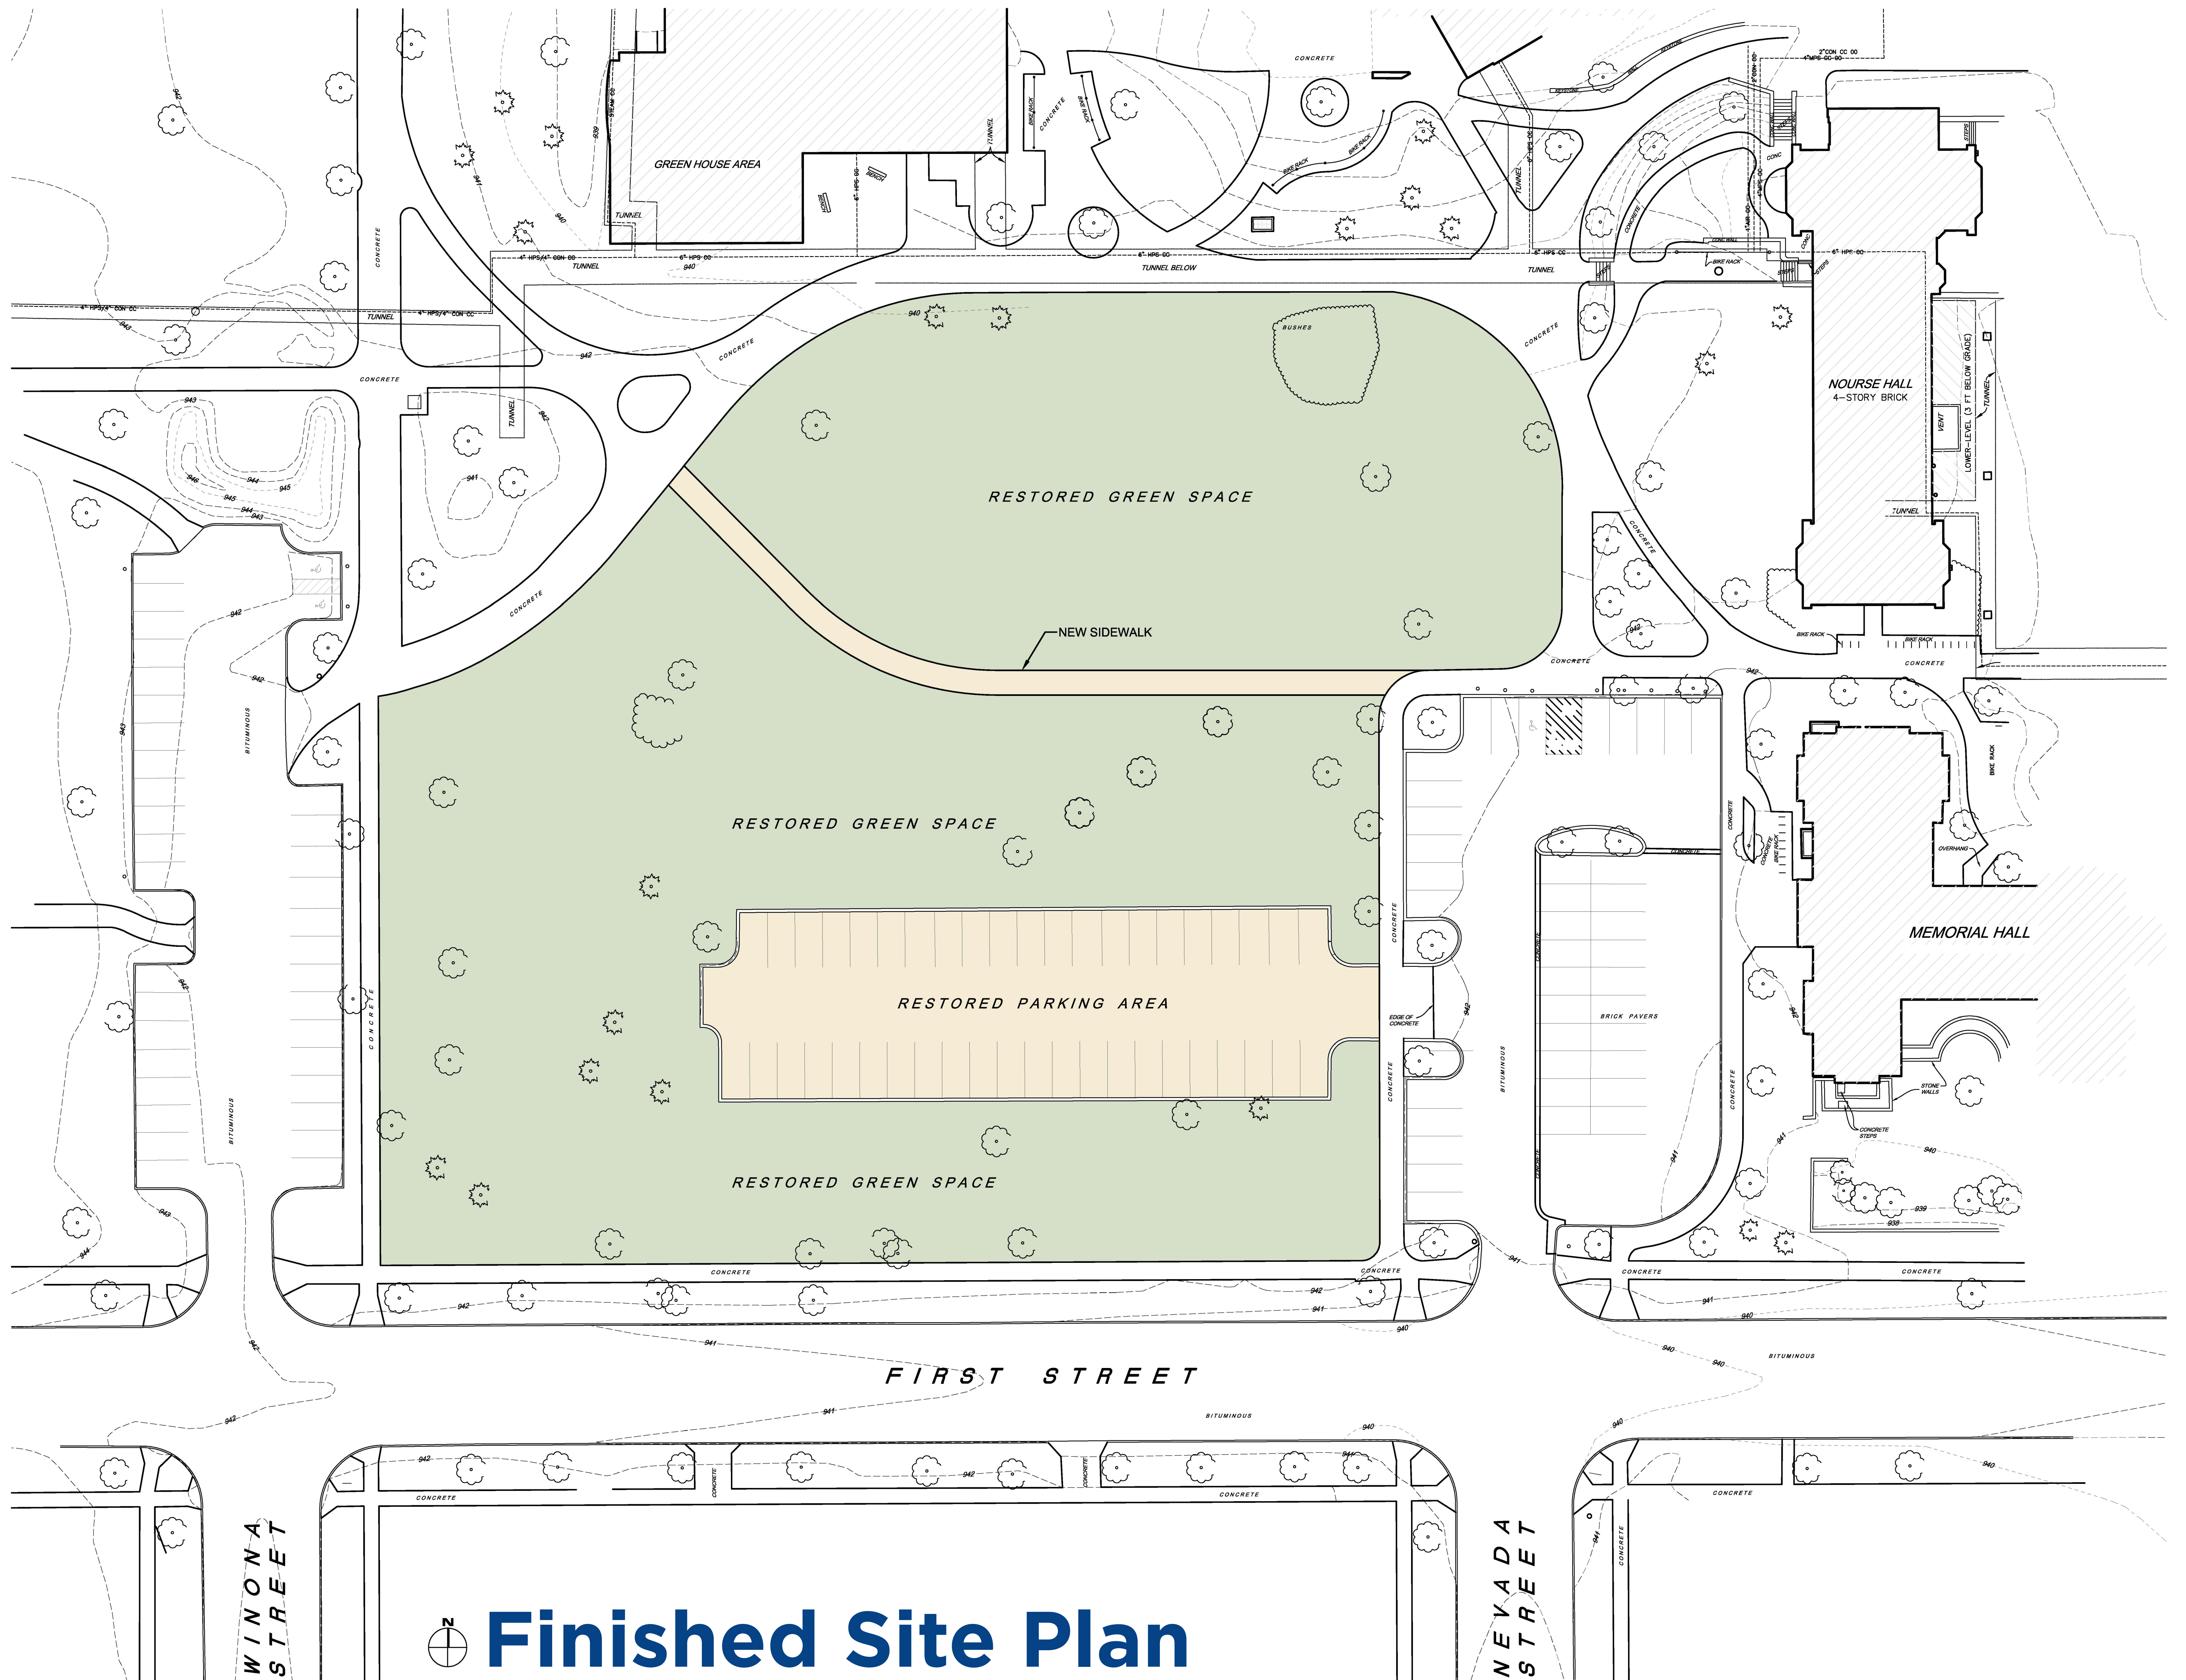

Finished Site Plan
